

Buenos Aires Progress Meeting Agenda 08.13.2009




AGENDA

Call In #: 1-720-356-2070 – Code # 142682

August 13th, 2009 1.00 PM to 3.00 PM

Progress Photographs

08.06.2009 Cafeteria View

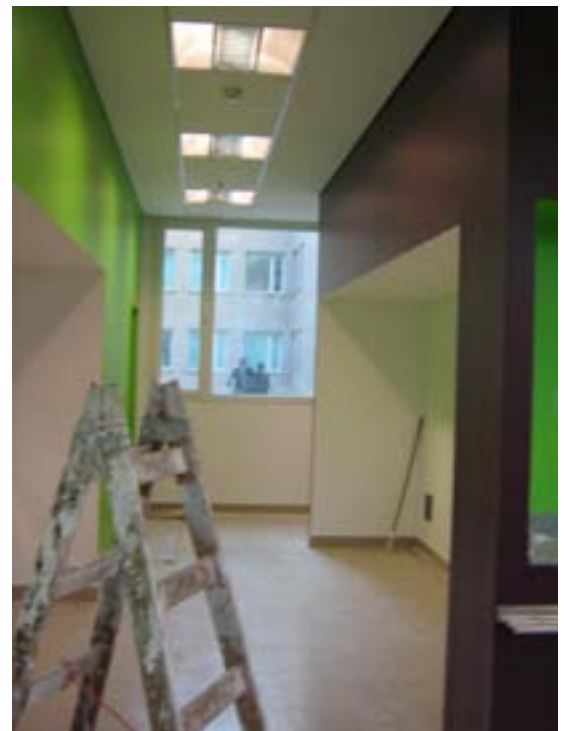

08.13.2009 Cafeteria View



Weekly milestones due today

CAFETERIA

- Special furniture – High table (50%)
- Stainless steel support for trays – Needs to be changed.
- HVAC interior covers (2 missing)
- Waiting for Cafeteria vendor to deliver his supplies.

LOOK AHEAD

- Review/Approve Costs for the Cafeteria Audio Video System – Target Install by end of August. – Waiting for final quotation. (The vendor explains that there is a lack of TVs in the local market)

PHASE II

- Chairs: we received a second alternative (Haworth). We are analyzing it, regarding cost and delivery date.
- Construction documents: Civil Works (from 7th to 10th) ready to be send on Tuesday 18-08. With the exception of 1st basement and plumbing installation.
- Modular glass Partitions: ready to be send on Tuesday 18-08
- Furniture: we received the confirmation that no privacy panels will be needed. Just to confirm if we'll ask for one white board to be share between two level 15 or one per each.
- Curtains definition: will move ahead with screen type but adding a glass mirror film on every window. (Should the films be required for the whole building?)
- We are expecting to received the final MEP Construction documents by the end of next week.
- Indico – Raised floor vendor is ready to begin placing the floor between 7th to 10th next week.
