

Buenos Aires Progress Meeting Agenda 12.30.2009

AGENDA

Call In #: 1-720-356-2070 – Code # 142682

December 30th, 2009 1.00 PM to 3.00 PM

Progress Photographs

12.24.2009 - 9th Floor View



12.30.2009 - 9th Floor View





12.24.2009 - 10th Floor View




12.30.2009 - 10th Floor View



12.24.2009 - Courtyard



12.30.2009 - Courtyard

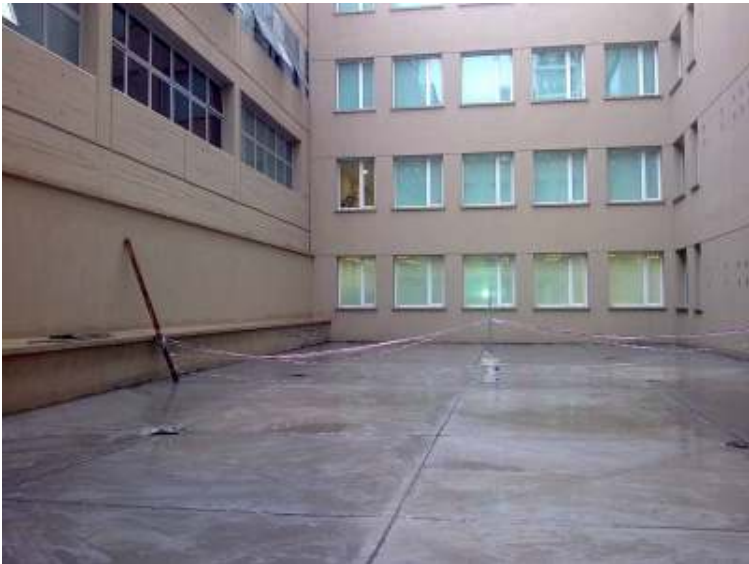

Weekly milestones due today

9th Floor – Substantial Completion December 30th

- Painting details – 95%
- Furniture – 100%
- Special furniture – 100%
- Curtains – 100%
- Finals details – 95%
- Final cleaning 100%
- Sun glare film – Pending (second week of January)

10th Floor – Substantial Completion January 20th

- Perimeter concrete flooring – 100%
- Cable trays below raised floor – 60%
- Lighting empty conduits above ceiling – 100%
- Empty conduits for fire detection – 100%
- Cabling below raised floor – 10%
- Lighting cabling – 50%
- Fire detection cabling – 25%
- CCTV cabling – 30%
- IT Patch Room works – 20%
- Dry walls structure – 100%
- First gypsum boards on dry walls partitions – 100%
- Dry wall isolation – 100%
- Second gypsum board on dry wall partitions – 80%
- Perimeter ceiling adjustment structure – 80%
- Perimeter ceiling adjustment gypsum boards – 70%
- Continuous ceiling structure – 85%
- Continuous ceiling board – 80%
- HVAC conduits – 60%
- HVAC interior units drain – 60%

LOOK AHEAD

- Sound Masking System: The system is installed and working from 7th to 9th floor.
- 9th Floor Temporary Chairs – Delivered
- Courtyard tiles to be completed with delivery of the 10th floor.
- 10th floor deliveries: Carpet – January 5th // Furniture- January 11th // IT Patch Room – January 8th

OPEN ISSUES

1. Vendor PO for Polycom to be revised in USD-Awaiting feedback from meeting with supplier and GSO.
2. Anticipating delivery of Permanent chairs late January.
3. Cafeteria Plasmas support placement – January 7th
