


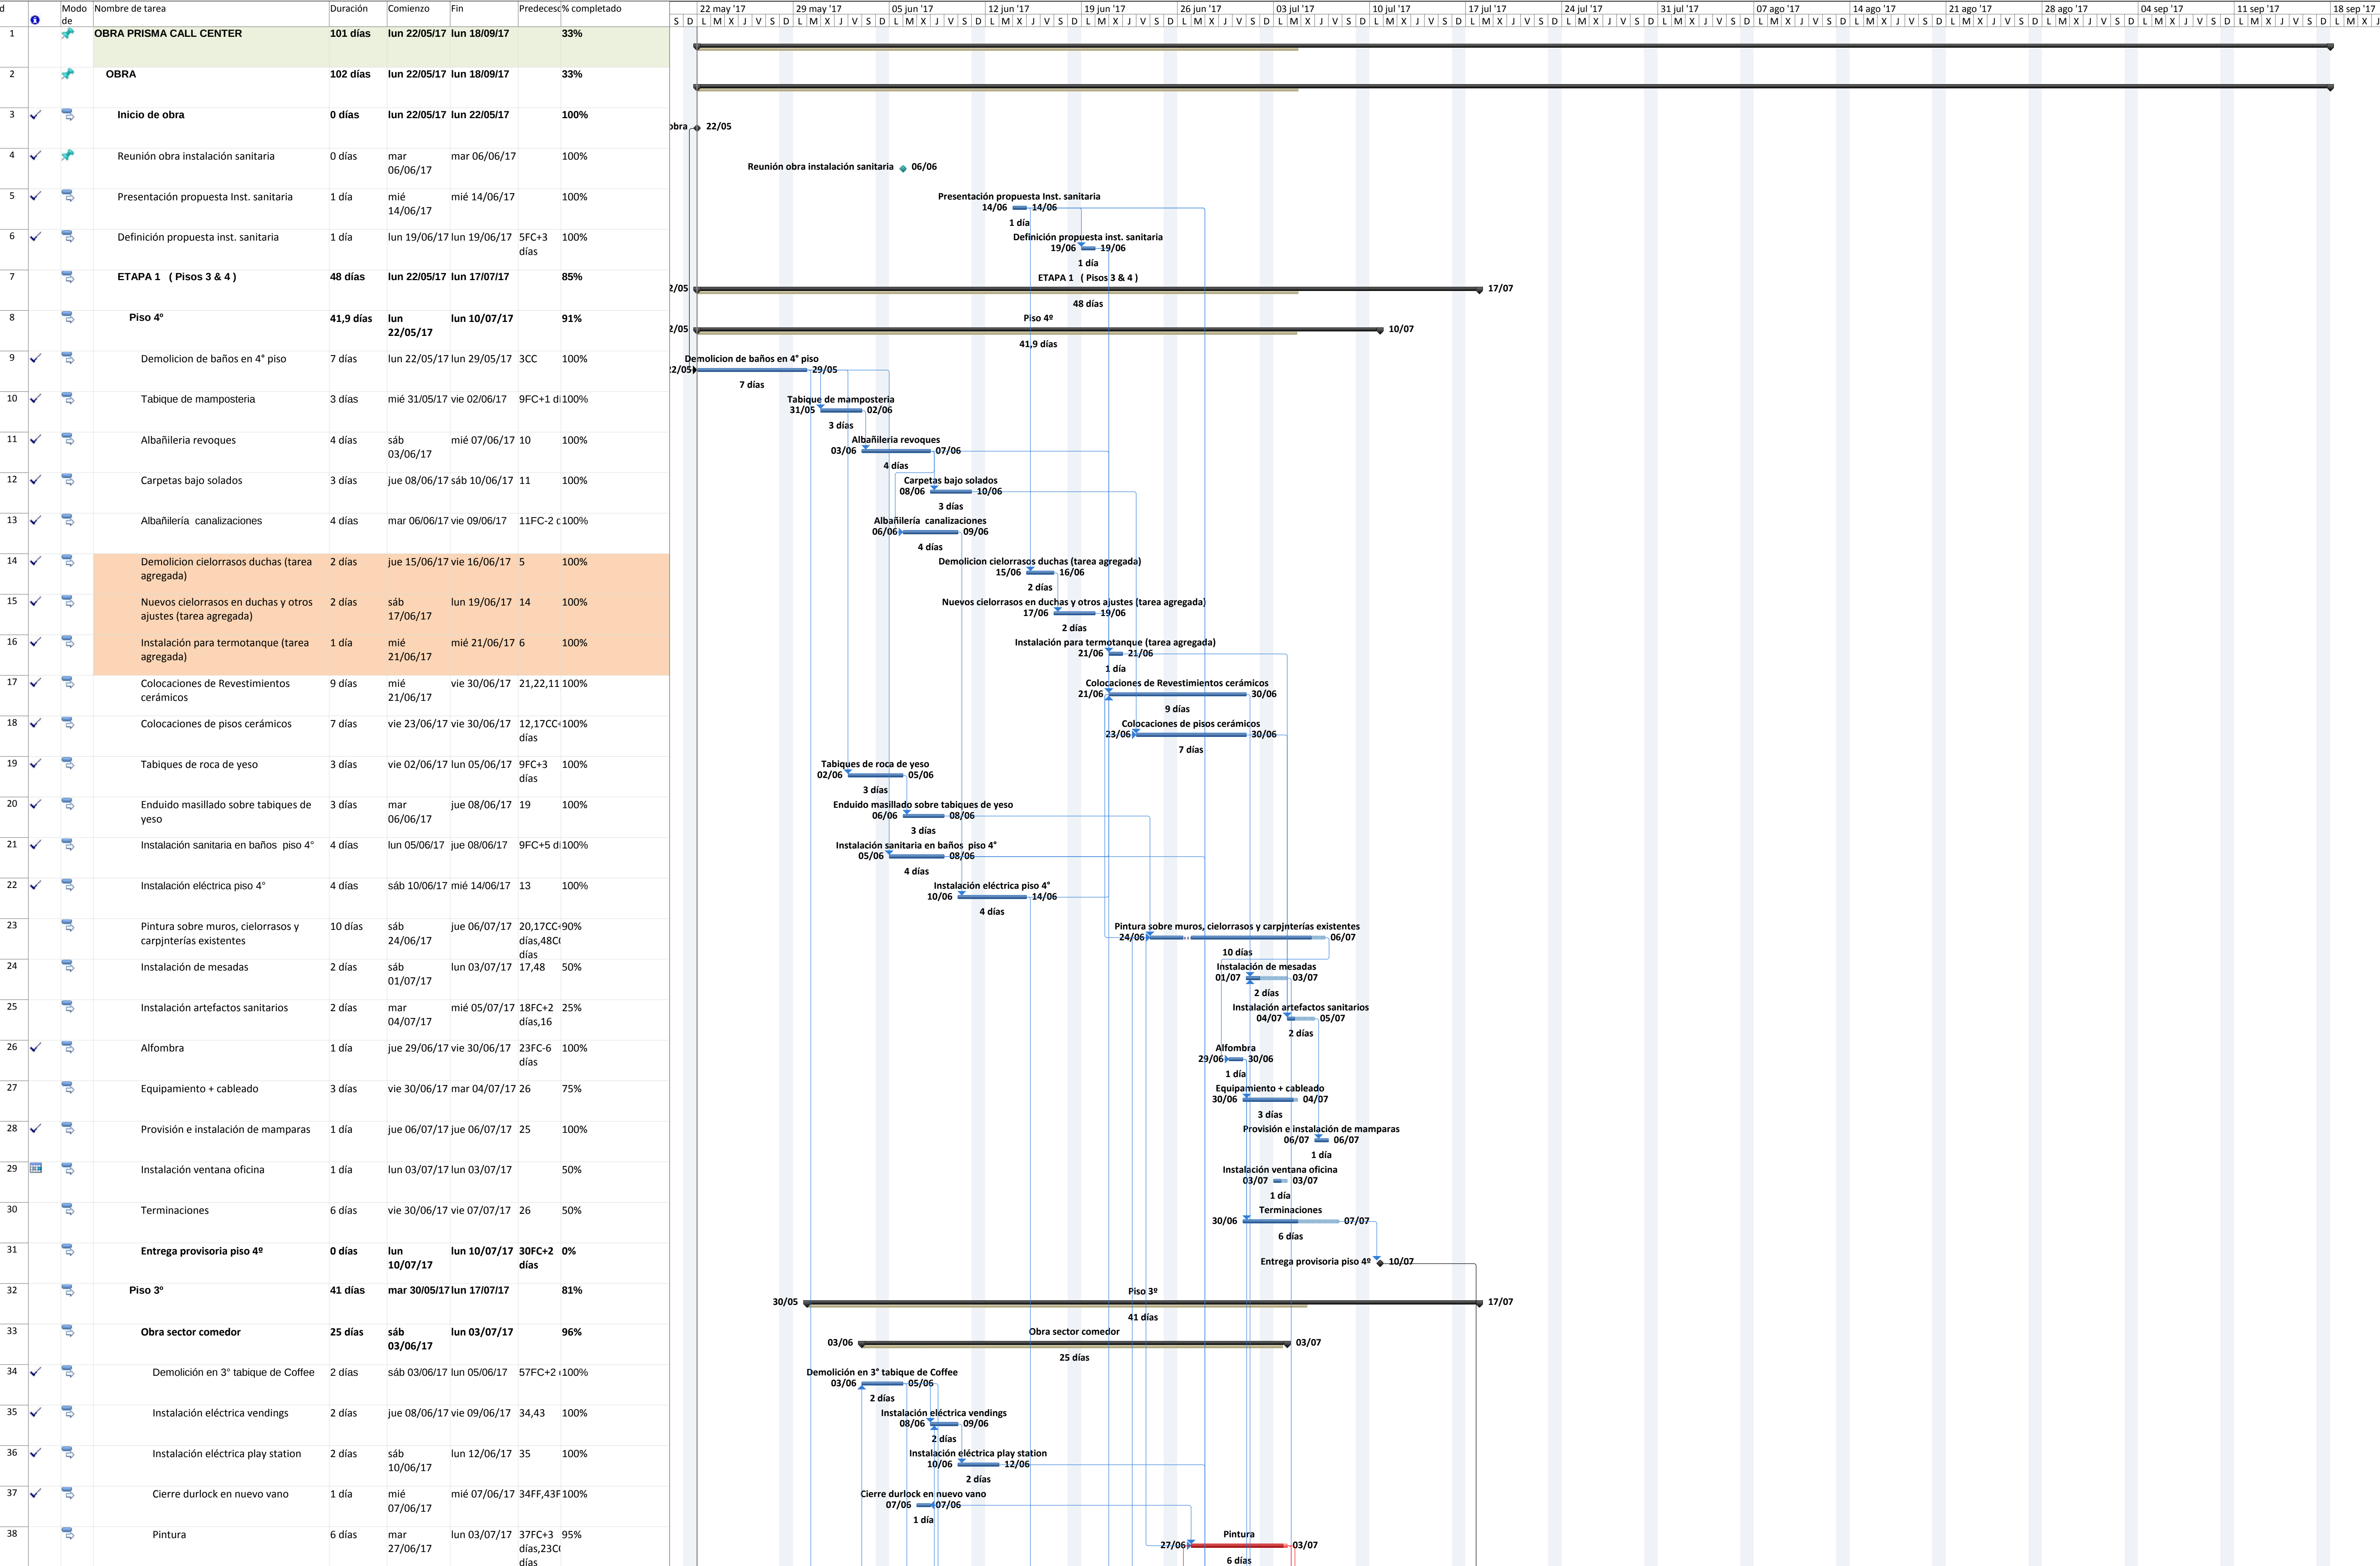

PRISMA CALL CENTER_cronograma obra ACTUALIZADO_v07-09-07-2017.mpp

	Modo de	Nombre de tarea	Duración	Comienzo	Fin	Predecesor	% completado		22 may '17	29 may '17	05 jun '17	12 jun '17	19 jun '17	26 jun '17	03 jul '17	10 jul '17	17 jul '17	24 jul '17	31 jul '17	07 ago '17	14 ago '17	21 ago '17	28 ago '17	04 sep '17	11 sep '17	18 sep '17
39		Terminaciones y ajustes	5 días	mié 28/06/17	lun 03/07/17	38FF,36	90%																			
40		Obra baños y enfermería	36 días	mar 30/05/17	mar 11/07/17		70%																			
41		Desmante de artefactos	2 días	mar 30/05/17	mié 31/05/17	57CC	100%																			
42		Demolicion de ceramicos pisos y revestimientos	4 días	jue 01/06/17	lun 05/06/17	41	100%																			
43		Demolición tabique de enfermería	2 días	mar 06/06/17	mié 07/06/17	34	100%																			
44		Albañilería (revoques)	5 días	mié 21/06/17	lun 26/06/17	42,6	100%																			
45		Carpetas bajo solados	2 días	lun 26/06/17	mar 27/06/17	44FC-1 día	100%																			
46		Ajustes en instalación sanitaria existente	5 días	mié 28/06/17	lun 03/07/17	5FC+10 días	0%																			
47		Instalacion sanitaria enfermería	2 días	mié 28/06/17	jue 29/06/17	21,5,46C	100%																			
48		Colocaciones de Revestimientos cerámicos	7 días	vie 23/06/17	vie 30/06/17	44FC-3 días	90%																			
49		Colocaciones de pisos cerámicos	5 días	sáb 01/07/17	jue 06/07/17	45,48	75%																			
50		Instalación sanitaria (colocación de artefactos)	2 días	vie 07/07/17	sáb 08/07/17	49	0%																			
51		Instalación eléctrica	4 días	lun 12/06/17	mar 27/06/17	44	100%																			
52		Colocacion mesadas	2 días	mar 04/07/17	mié 05/07/17	48,24	25%																			
53		Colocacion piso vinilico	3 días	vie 30/06/17	mar 04/07/17	26	50%																			
54		Pintura sobre muros, cielorrasos y carpinterías existentes	5 días	mar 04/07/17	sáb 08/07/17	38	50%																			
55		Armado de mobiliario	2 días	lun 10/07/17	mar 11/07/17	54,53	50%																			
56		Obra oficina	33 días	mar 30/05/17	vie 07/07/17		99%																			
57		Demolición y retiro equipamiento operativo	2 días	mar 30/05/17	mié 31/05/17	9	100%																			
58		Instalación eléctrica	5 días	jue 15/06/17	mié 21/06/17	57,22	100%																			
59		Cableado estructurado	5 días	mar 20/06/17	sáb 24/06/17	58FC-1 día	100%																			
60		Pintura sobre muros, cielorrasos y carpinterías existentes	7 días	mar 27/06/17	mar 04/07/17	38CC	95%																			
61		Cierre piso tecnico y nivelacion	1 día	vie 23/06/17	vie 23/06/17	59FC-2 días,58	100%																			
62		Alfombra	2 días	sáb 24/06/17	lun 26/06/17	61	100%																			
63		Entrega de muebles de Cerrito 740	0 días	lun 26/06/17	lun 26/06/17	62	100%																			
64		Armado de equipamiento operativo	3 días	mar 27/06/17	jue 29/06/17	63	100%																			
65		Equipamiento / cableado	4 días	lun 03/07/17	jue 06/07/17	64	100%																			
66		Certificacion de puestos	1 día	vie 07/07/17	vie 07/07/17	65	100%																			
67		Terminaciones y ajustes	7 días	lun 10/07/17	lun 17/07/17	65CC,50,50%																				
68		Entrega provisoria piso 3º	0 días	lun 17/07/17	lun 17/07/17	67	0%																			
69		Entrega Provisoria ETAPA 1	0 días	lun 17/07/17	lun 17/07/17	31,68	0%																			
70		ETAPA 2 (Pisos 1 & 2)	68 días	lun 10/07/17	mar 26/09/17	39,67FC-0% días																				
71		Piso 2º	66 días	lun 10/07/17	sáb 23/09/17		0%																			
107		Piso 1º	68 días	lun 10/07/17	mar 26/09/17		0%																			
143		Entrega Provisoria ETAPA 2	0 días	mar 26/09/17	mar 26/09/17	142,106	0%																			
