Id		Nombre de tarea	Duración	Comienzo	Fin
0		**Plan de obra MERRILL LYNCH**	**45 días**	**vie 14-11-08**	**vie 02-01-09**
1		**START UP**	**45 días**	**vie 14-11-08**	**vie 02-01-09**
2		Kick off	0 días	vie 14-11-08	vie 14-11-08
3		**Demolitions on the Server room area**	**4 días**	**sáb 15-11-08**	**mar 18-11-08**
4		Tiled ceiling	1 día	sáb 15-11-08	sáb 15-11-08
5		Gypsum board ceiling	2 días	sáb 15-11-08	dom 16-11-08
6		Existant pavement removal	2 días	lun 17-11-08	mar 18-11-08
7		**Gypsum board partitions and ceilings on the Server roon area**	**18 días**	**mié 19-11-08**	**sáb 06-12-08**
8		Metal structure	6 días	mié 19-11-08	lun 24-11-08
9		First side gypsum board	3 días	mar 25-11-08	jue 27-11-08
10		Second side gypsum board	3 días	lun 01-12-08	mié 03-12-08
11		Gypsum board ceilings	3 días	jue 04-12-08	sáb 06-12-08
12		**Painting on the Server room area**	**8 días**	**mar 09-12-08**	**mar 16-12-08**
13		Plaster in new drywall partitions	3 días	mar 09-12-08	jue 11-12-08
14		Paint in drywall partitions	5 días	vie 12-12-08	mar 16-12-08
15		Plaster in gypsum board ceiling	3 días	mar 09-12-08	jue 11-12-08
16		Paint in ceiling	2 días	vie 12-12-08	sáb 13-12-08
17		**Pavement on the Server room area**	**2 días**	**mié 17-12-08**	**jue 18-12-08**
18		Vinyl tiled pavement installation	2 días	mié 17-12-08	jue 18-12-08
19		**Demolition on the Open Plan**	**35 días**	**vie 14-11-08**	**sáb 20-12-08**
20		Existant workstations movement	1 día	vie 14-11-08	vie 14-11-08
21		Drywall and glazed partitions	2 días	sáb 15-11-08	dom 16-11-08
22		Tiled ceiling	2 días	lun 17-11-08	mar 18-11-08
23		Removal of existant carpet	1 día	sáb 20-12-08	sáb 20-12-08
24		**Gypsum board partitions and ceilings**	**19 días**	**lun 17-11-08**	**vie 05-12-08**
25		Metal structure	2 días	lun 17-11-08	mar 18-11-08
26		First side gypsum board	2 días	mié 19-11-08	jue 20-11-08
27		Second side gypsum board	2 días	lun 01-12-08	mar 02-12-08
28		Gypsum board ceilings	3 días	mié 03-12-08	vie 05-12-08
29		**Fire Protection System**	**13 días**	**lun 17-11-08**	**sáb 29-11-08**
30		Changes in fire proyection system	4 días	lun 17-11-08	jue 20-11-08
31		Duct work for sensors	4 días	vie 21-11-08	lun 24-11-08
32		Sensors wiring	2 días	mar 25-11-08	mié 26-11-08
33		Sensors installation	2 días	jue 27-11-08	vie 28-11-08
34		Commissioning	1 día	sáb 29-11-08	sáb 29-11-08
35		**Tiled ceiling**	**5 días**	**mié 03-12-08**	**mar 09-12-08**
36		Grid installation	3 días	mié 03-12-08	vie 05-12-08
37		Tiles installation	2 días	sáb 06-12-08	mar 09-12-08
38		**Doors**	**5 días**	**mié 03-12-08**	**mar 09-12-08**
39		Installation	3 días	mié 03-12-08	vie 05-12-08
40		Plaster and paint	2 días	sáb 06-12-08	mar 09-12-08
41		**Painting on Open Area**	**5 días**	**mié 03-12-08**	**mar 09-12-08**
42		Plaster in new drywall partitions	2 días	mié 03-12-08	jue 04-12-08
43		Paint in drywall partitions	3 días	vie 05-12-08	mar 09-12-08
44		Plaster in gypsum board ceiling	1 día	sáb 06-12-08	sáb 06-12-08
45		Paint in ceiling	1 día	mar 09-12-08	mar 09-12-08
46		**Pavement on Open Area**	**19 días**	**mié 03-12-08**	**mar 23-12-08**
47		Removal of existant furniture MONEY TABLE	1 día	sáb 20-12-08	sáb 20-12-08
48		Carpet installation	1 día	sáb 20-12-08	sáb 20-12-08
49		Baseboards installation	3 días	dom 21-12-08	mar 23-12-08
50		Installation of existant tiled pavement	2 días	mié 03-12-08	jue 04-12-08
51		**Electrical System and Structured Cabling**	**37 días**	**vie 14-11-08**	**lun 22-12-08**
52		Removal of existant duct work	2 días	lun 17-11-08	mar 18-11-08
53		Temporary existant wiring	1 día	vie 14-11-08	vie 14-11-08
54		Ductwork in partitions	3 días	vie 28-11-08	dom 30-11-08
55		Ductwork over ceiling	2 días	mié 19-11-08	jue 20-11-08
56		Electric and structured wiring	7 días	lun 01-12-08	mar 09-12-08
57		Sockets and switch installation	5 días	mié 10-12-08	dom 14-12-08
58		Relocation and installation of light fixtures	2 días	dom 14-12-08	lun 15-12-08
59		Arrival of new racks	1 día	vie 14-11-08	vie 14-11-08
60		Works on rack	8 días	jue 04-12-08	sáb 13-12-08
61		UPS installation	7 días	lun 15-12-08	dom 21-12-08
62		Works on electric pannels	5 días	mié 10-12-08	dom 14-12-08
63		Duct work and wiring in MONEY TABLE	1 día	dom 21-12-08	dom 21-12-08
64		Certification and labelling	8 días	lun 15-12-08	lun 22-12-08
65		Shut down of existant workstations	1 día	jue 11-12-08	jue 11-12-08
66		Connectivity to new server	2 días	vie 12-12-08	sáb 13-12-08
67		Old server disarmament	2 días	dom 14-12-08	lun 15-12-08
68		Removal of equipment	1 día	mar 16-12-08	mar 16-12-08
69		**HVAC System**	**30 días**	**lun 17-11-08**	**jue 18-12-08**
70		Removal of existant units	2 días	lun 17-11-08	mar 18-11-08
71		Relocation of existant units	2 días	mié 19-11-08	jue 20-11-08
72		Installation of new units for the server room	2 días	vie 21-11-08	sáb 22-11-08
73		Duct work for units	2 días	lun 17-11-08	mar 18-11-08
74		Duct work for thermostats	1 día	vie 28-11-08	vie 28-11-08
75		Installation of diffusers	1 día	dom 14-12-08	dom 14-12-08
76		Duct work	2 días	vie 21-11-08	sáb 22-11-08
77		Thermostats wiring	1 día	mar 09-12-08	mar 09-12-08
78		Thermostats installation	1 día	mié 17-12-08	mié 17-12-08
79		Electric connectivity	2 días	lun 15-12-08	mar 16-12-08
80		Removal and installation of existant unit in server room	2 días	mar 16-12-08	mié 17-12-08
81		Commissioning	1 día	jue 18-12-08	jue 18-12-08
82		**FURNITURE**	**4 días**	**vie 19-12-08**	**lun 22-12-08**
83		Arrival	1 día	vie 19-12-08	vie 19-12-08
84		Installation of MONEY TABLE	2 días	sáb 20-12-08	dom 21-12-08
85		Installation of Back office	1 día	lun 22-12-08	lun 22-12-08
86		**FINAL CLEANING AND PUNCH LIST**	**8 días**	**mar 23-12-08**	**vie 02-01-09**
87		Final Cleaning	2 días	mar 23-12-08	mié 24-12-08
88		Punch List	6 días	vie 26-12-08	vie 02-01-09

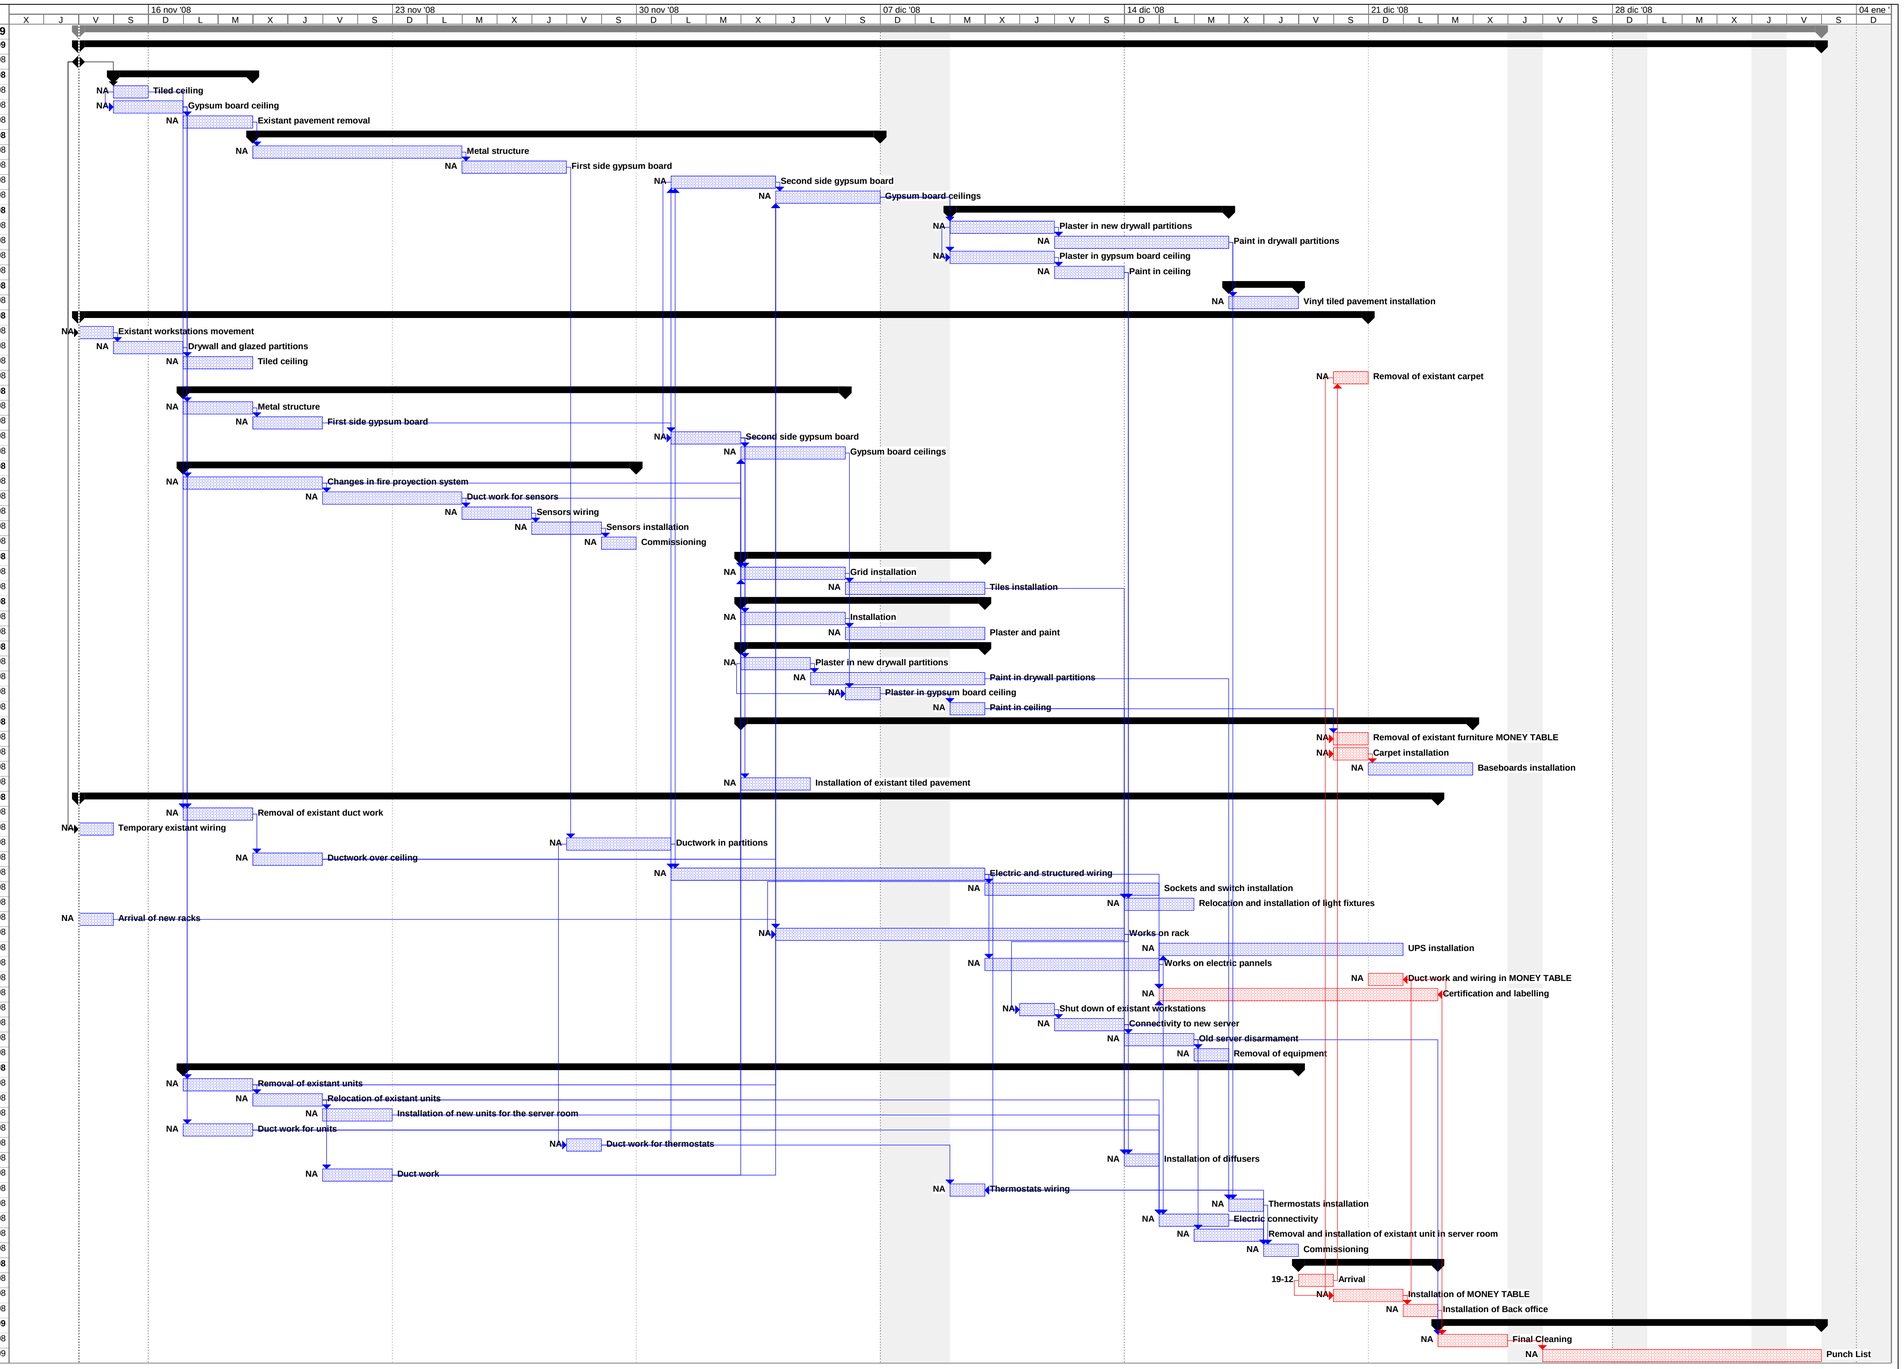

Proyecto: Plan de obra MERRILL
Fecha: vie 14-11-08

Tarea | Progreso | Resumen | Tarea crítica resumida | Progreso resumido | Tareas externas | Agrupar por síntesis
Tarea crítica | Hito | Tarea resumida | Hito resumido | División | Resumen del proyecto | Fecha límite
